

**LEGEND**

**Tree Inventory**  
Refer to Table 1 of the report dated 14 November 2023 for the complete tree inventory information. Trees measuring 10cm DBH and greater on and within 5x metres of the subject property were included in the inventory.

**Trees Removals**  
The removal of 27 trees will be required to accommodate the proposed development, as indicated with RED circles.

**Tree Preservation**  
The preservation of the remaining trees and polygons will be possible with the use of appropriate tree protection measures. Trees identified for preservation are indicated with GREEN circles. Tree protection measures must be implemented prior to the commencement of the proposed works. Required tree preservation fencing is indicated in MAGENTA. Refer to the tree preservation fence detail and the Tree Protection Plan Notes.

- Tree Label (GREEN), Preservation Recommended X
- Tree Label (RED), Removals Required X
- Minimum Tree Protection Zone (mTPZ) of Tree Identified for Preservation (MAGENTA line) ○
- Minimum Tree Protection Zone (mTPZ) of Tree Identified for Removal (RED line) ○
- Tree Location Estimated by KFC ○
- Location of Required Tree Preservation Fencing (tick MAGENTA) ┆
- Location of Root Pruning Trench (tick CYAN) ┆
- Tree Does Not Exist X

**Specifications for the Protection and Preservation of Existing Vegetation**

- The following notes are to be included on all tree preservation plans:
1. No existing trees, which are to remain, shall be fully protected with hoarding to City standards, erected beyond their root zone or to the satisfaction of the Front and Sidewalk Control Permit, to the satisfaction of the Community Services Department. Groups of trees and other existing plantings to be protected, shall be treated in the manner with hoarding around the entire planting. Areas within the protected landing shall remain undisturbed and shall not be used for the storage of building materials or equipment.
  2. No tying cables shall be wrapped around or installed in trees. Surplus soil, equipment, decks or materials shall not be used over root systems of the trees within the protective landing. No contaminants shall be dumped or flushed where feeder roots of trees exist.
  3. The developer or his/her agents shall take every precaution necessary to prevent damage to trees or shrubs to be retained.
  4. Where limbs or portions of trees are removed to accommodate construction work, they shall be removed carefully in accordance with accepted arboricultural practices.
  5. Where root systems of trees are exposed directly adjacent to or damaged by construction work, they shall be trimmed neatly and the area backfilled with appropriate material to prevent desiccation.
  6. Where necessary, the trees shall be given an overall pruning to restore the balance between roots and top growth or to restore the appearance of the trees.
  7. Trees that have died or have been damaged beyond repair, shall be removed and replaced by the owner at the developer's own expense with trees of a size and species as approved by the Community Services Department.
  8. If grades around trees to be protected are likely to change, the owner shall be required to take such precautions as dry well, milling wells and root feeding to the satisfaction of the Community Services Department.

No.	Issue/Revisions	Date	By
1	Report Submission	14 Nov '23	HNH

Base Data: R. A. S. Surveying (Survey), Cooper (Site Plan)


**KUNTZ FORESTRY CONSULTING Inc.**  
146 Lakeshore Road West  
PO Box 1207 Lakeshore W PO  
Oakville ON L6K 0S3  
T: 288.637.971  
e: consultant@kuntzforestry.ca  
www.kuntzforestry.ca

**Dumpar**  
105 Six Point Road  
Etobicoke, Ontario M8Z 2X3

Property  
**2620 Chalkwell Close**  
Mississauga, Ontario

**Tree Inventory and Preservation Plan**

Project	P3982	Figure	<b>1</b>
Date	14 November 2023		
Scale	1:400		

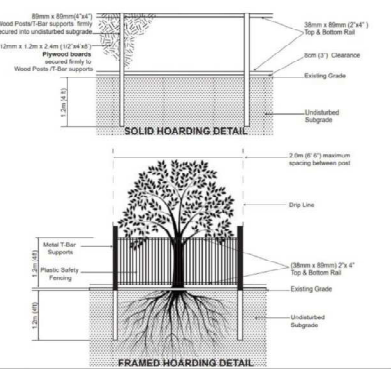

- NOTES:**
1. Hoarding details to be determined following initial site inspection.
  2. Private tree hoarding to be approved by Development & Design.
  3. City tree hoarding to be approved by Community Services Dept.
  4. Hoarding must be installed, installed and maintained by the applicant throughout all phases of construction. Inspection must be conducted by the Development and Design Division prior to removing any/all private hoarding.
  5. Do not allow water to collect and pond behind or within hoarding.
  6. T-bar supports are acceptable alternative to dead posts. U-shaped metal supports will not be accepted.
  7. If wood must be utilized for solid hoarding, OSB/Chipboard will not be accepted for solid hoarding. Plywood sheets must be installed on "construction" side of frame.
  8. Applicant is responsible to ensure utility locations are completed within city boulevard prior to installing framed hoarding.

**MISSISSAUGA**

**Tree Protection Zone (TPZ)**  
BY-LAW #

No construction activities, including grade changes, storage of materials or equipment, dumping, excavation is permitted within this TPZ

This tree protection barrier must remain in good condition and must not be removed or altered without the authorization of City of Mississauga, Urban Forestry.

Concerns or inquires regarding this TPZ can be directed to:

**(3-1-1)** Dial 3-1-1 or 905-615-4311 outside city limits

